

Information Technology

To: byfieldwater@comcast.net
Subject: RE: Review of Application for the Village at Cricket Lane - 55R Pearson Drive, Byfield

From: byfieldwater@comcast.net [<mailto:byfieldwater@comcast.net>]
Sent: Thursday, March 05, 2020 10:02 AM
To: IT/Communications/Webmaster
Subject: Re: Review of Application for the Village at Cricket Lane - 55R Pearson Drive, Byfield

Hi Susan,

Byfield Water has reviewed the plans as submitted for this development. The district is not opposed to the development and feel we have adequate water supply for the 24 new homes. However it will be necessary for the developer to meet with us to go over items in the plans that we have questions on. We have not met with anybody on this new development as of yet. There are specifications the district requires pertaining to new water mains, hydrants and service connections that we want to be sure the developer is aware of.

Thanks,

Paul Colby
Director, BWD

ARTEC SPRINKLER CORPORATION
90 Progress Avenue Suite 2 - Tyngsboro, MA 01879
Telephone: 978.459.2568 Fax: 978.453.4473
License #001489


HYDRANT WATERFLOW INSPECTION RESULTS

Test Date: 9-11-2020 Time of Test: 9:00

Test Site: The Villages at Cricket Lane

Address: Person Dr

Newbury Mass

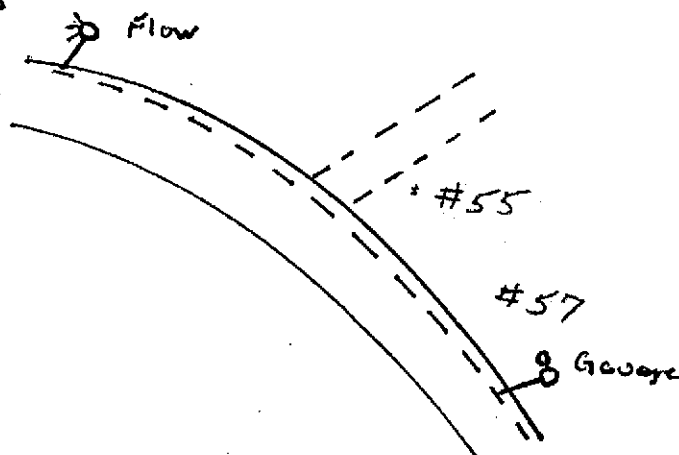

Hydrant: A Static: 80

B Residual: 60

Flow: 1050

City Main: 8"

Elevation: Even

Pilot: 38

Hydrant butt Coefficient: 0.7

Type: 2 1/2

Available at 20 PSI: _____

Water Dept: Py Field Water

Technician Test Performed by: Gerard Guillette

Remarks:
